# Construction Manager's Update

April 16, 2025





## Blue Ridge Community College MRTS Projects

## Blue Ridge Community College Facilities Building

- Programming is underway
- Henderson County staff is working closely on programming with BRCC and Clark Nexsen




#### Henderson County Public Schools MRTS Projects



#### West Henderson High School Renovation & Addition



- Thank you to all who attended the ribbon cutting on 4/4
- We are pleased to report that this project was completed on-time and under-budget

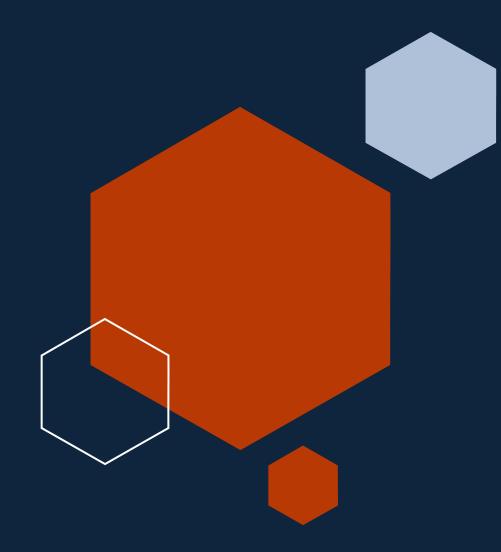


Henderson County Capital Projects



#### Henderson County AG Services Building

- Programming process is underway
- Henderson County Staff, MPS, and all stakeholders are working collaboratively on programming

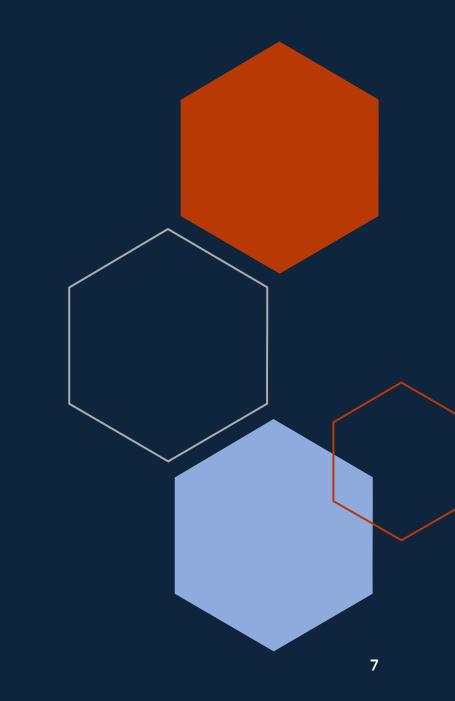

## Ag Services Schedule




17<sup>th</sup> Site Kickoff
Meeting

• 18<sup>th</sup>-Programming Kickoff meeting

#### June

 2<sup>nd</sup>-Programming documents presented to BOC



BOC

#### Medical Office Buildings






### Medical Office Buildings


- Staff is progressing through the Design Development phase at the Spartanburg Hwy. location
- Schematic Design is being revised and reprogrammed for the Mills River site
- The Board will be presented a SD Deliverable update, on the Mills River location, in the upcoming months.




#### Medical Office Buildings: Spartanburg Highway Schedule



#### Medical Office Buildings: Mills River Schedule

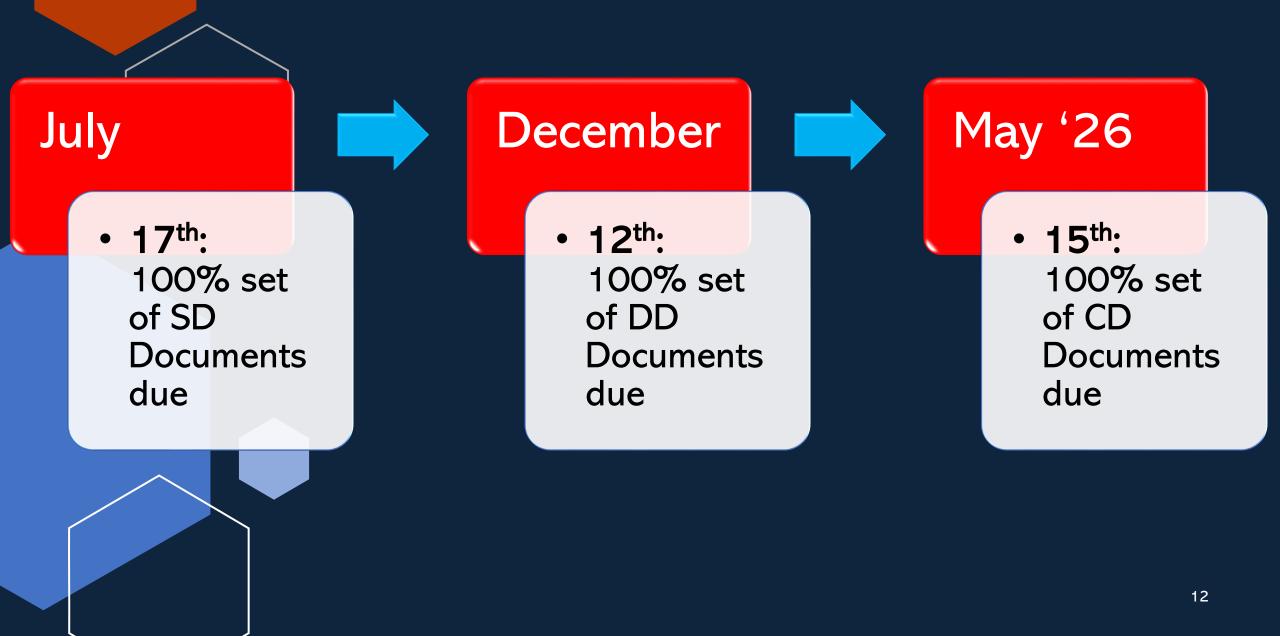

#### Henderson County JCAR Project

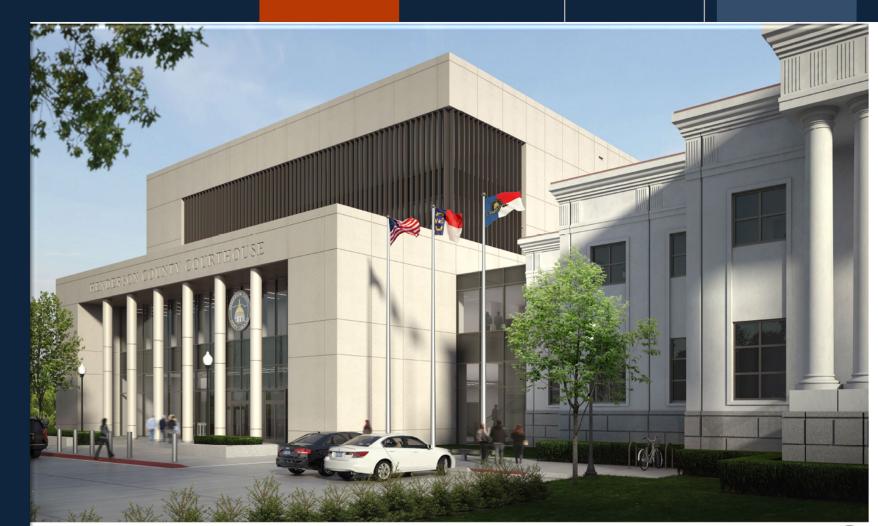

January 23, 2025 HENDERSON COUNTY JUDICIAL CENTER Hendersonville, NC PERSPECTIVES South-West Entrance View





**DETENTION CENTER - NEW VEHICULAR SALLYPORT** 



January 23, 2025 HENDERSON COUNTY JUDICIAL CENTER Hendersonville, NC

DETENTION CENTER RENDERINGS



## JCAR: Detention Schedule

April 4<sup>th</sup>: 100% CD Deliverable received from Fentress Architects



July 16<sup>th</sup>: GMP Submittal for BOC Approval



September 1<sup>st</sup>: NTP on construction, pending LGC funding approval



## JCAR: Courts Schedule

March			
21 <sup>st</sup> :	August		
NTP: CD Phase	20 <sup>th</sup> :	December	
	Potential early release site/civil package presented to BOC	19 <sup>th</sup> :	
		100% CD Deadline, full GMP to follow	
	DOC		

#### Henderson County Sports Complex



Thank you to all who attended the Ground-Breaking ceremony on March 31st

Photo Credit: Mike Morgan

#### Henderson County Sports Complex



Staff is excited to begin construction on this project







### Construction Manager's Update

## Any Questions?
