

FACILITIES MAINTENANCE AND REPAIR, TECHNOLOGY AND SECURITY INITIATIVES


HENDERSON COUNTY PUBLIC SCHOOLS

February, 2023


Detailed Project Report

PROJECT		FY23 BOC APPROVED		\$ EXPENDED/ ENCUMBERED		% EXPENDED/ ENCUMBERED	I PROJECT STATUS		TOTAL REMAINING	
E1										
	ntary Schools									
ES-4	Upward - Entrance/Cafeteria	\$	2,072,584	\$	104,615	5%	Not Started	\$	1,967,969	
SC-1	Security Cameras	\$	843,795	\$	843,845	100%	In Progress	\$	(50	
Middle	Schools									
SC-1	Security Cameras	\$	247,365	\$	149,755	61%	In Progress	\$	97,610	
High Ca	chools									
High So	Security Cameras	\$	297,500	\$	186,925	63%	In Progress	\$	110,575	
RF-1	East - Gym Roof Replacement	\$	7,378	\$	7,378	100%	Complete	\$	((
HS-5	West - Y - Hall Classroom Roofs	\$	162,050	\$	162,050	100%	Complete	\$	((
HS-6	West - V - Hall Classroom Roofs	\$	18,179	\$	18,179	100%	Complete	\$	((
HS-7	West - Renovations and Additions	\$	5,000,000	\$	284,450	6%	Not Started	\$	4,715,550	
System	n Wide Projects									
SW-4	Project Empower Chromebooks	\$	300,000	\$	-	0%	In Progress	\$	300,000	
SW-U	Unallocated/Contingency	\$	45,081	\$	-	0%	Not Started	\$	45,08	
PVAE-1	Paving - Unspecified	\$	165,000	\$	13,000	8%	In Progress	\$	152,000	
MW-1	Maintenance Warehouse A&E	\$	3,267	\$	2,716	83%	Complete	\$	55:	
MW-2	Maintenance Warehouse	\$	91,460	\$	85,941	94%	Complete	\$	5,51	
AERF-1	. Roofing A&E	\$	4,280	\$	4,013	94%	Complete	\$	26	
BG-1	Bus Garage Planning & Design	\$	19,800	\$	19,800	100%	In Progress	\$	-	
BG-2	Bus Garage Construction	\$	-	\$		0%	Not Started	\$	-	
TOTAL		\$	9,277,739	\$	1,882,667	20%		\$	7,395,07	

At A Glance - Summary Report

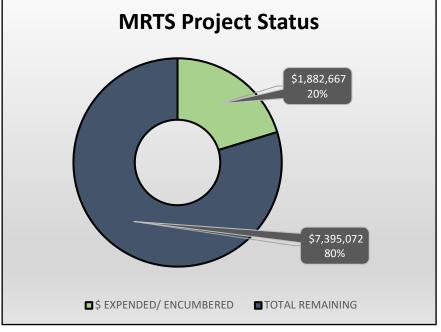





TO	TAL REMAINING
	\$7,395,072
